


INTERSECTION RENEWAL KOROIT & KEPLER STREET


WEEKS 5 - 7

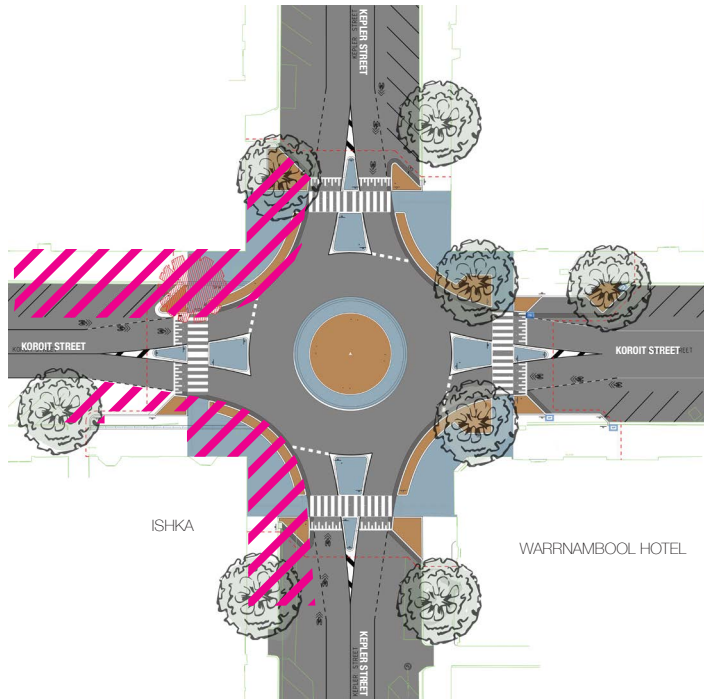

Works involved

- Demolition of footpath and kerb on the north-west corner (weeks 5 & 6)
- Installation of drainage and other services including power, water, communications and irrigation on the north west corner (week 6)
- Basalt paving on south-west corner (weeks 6 & 7)


WEEKS 6 – 10 From July 15

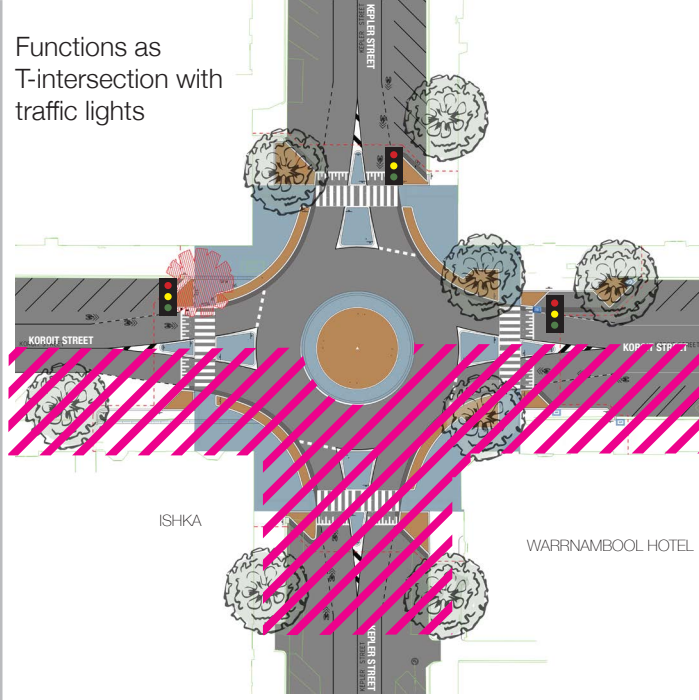

Works involved

- Demolition of road pavement
- Wannon Water – water main upgrade
- Service upgrade
- Building splitter islands, pedestrian crossings and road pavement
- Paving centre island
- Application of foam bitumen


Weeks 11 & 12

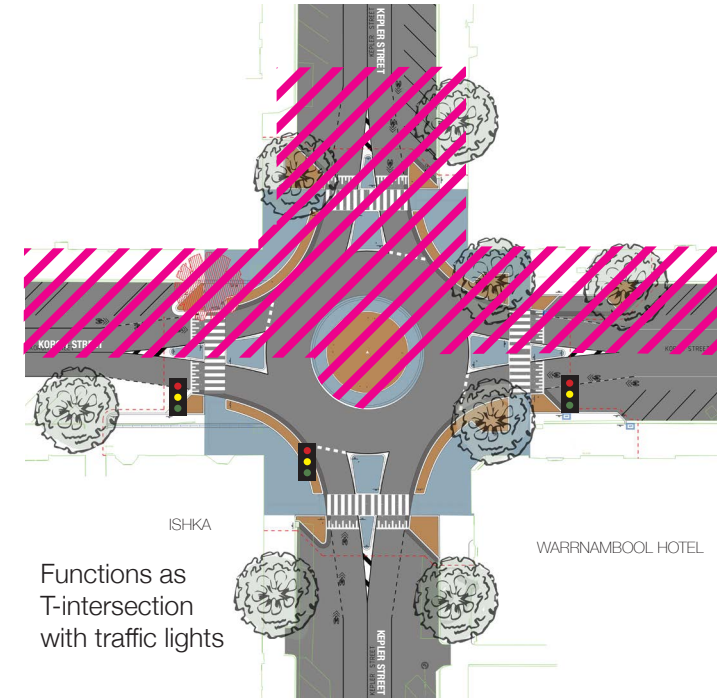

Works involved

- Building pedestrian crossings, splitter islands and ramps on the north side of the intersection
- Application of foam bitumen

WEEK 13 (approximately)

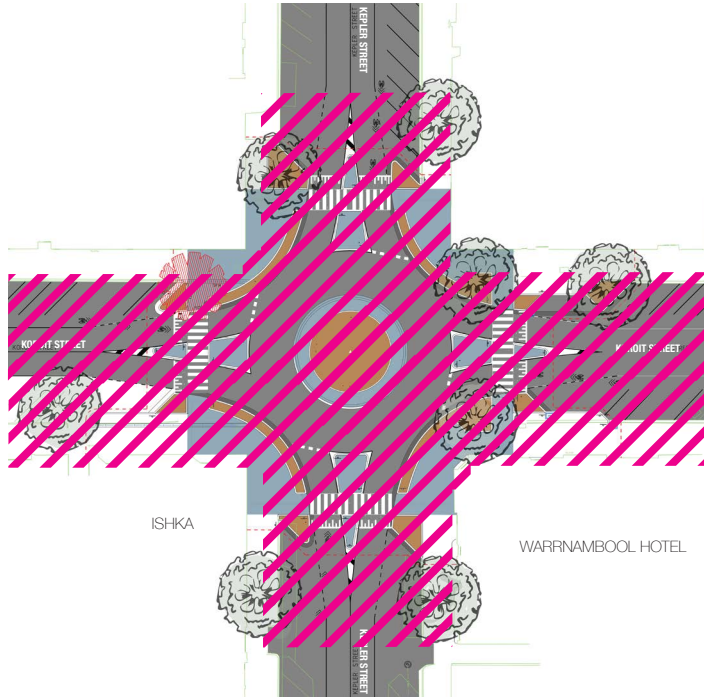

Works involved

- Excavation, preparation for new road surface
- Application of asphalt
- Signage
- Garden beds and irrigation
- First round of line-marking
